



Grassy Plains Daycare

34310 Keefe's Landing Rd

Progress Photos to:

Week of May 9, 2024

PRD Construction Ltd

1253 5th Avenue, Prince George, BC, V2L 3L3

Michael Duck

250.617.2499


michael@prdconstruction.ca



Door Frames are installed and being painted




Walls getting first colour coats

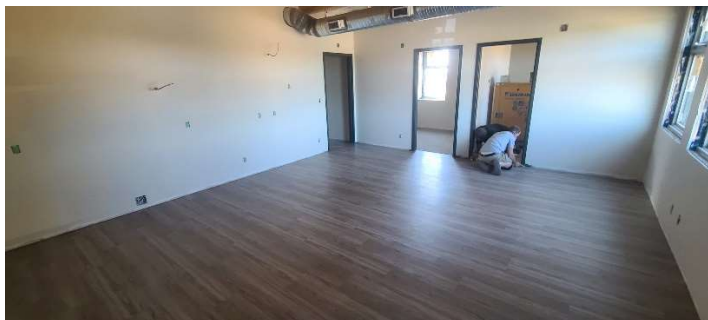

Flooring Installation in the foods / staff room



Another angle of the foods / staff room flooring

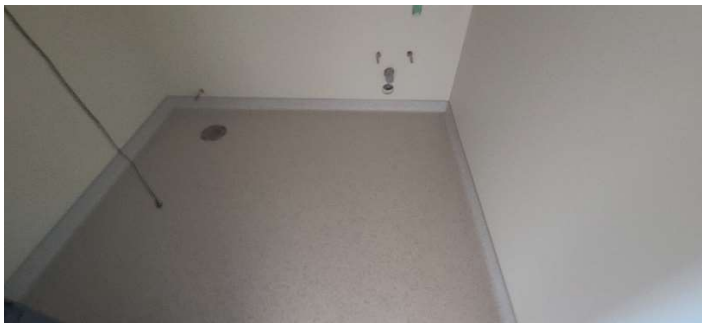

Areas subject to moisture, like this washroom, receive sheet vinyl flooring with a continuous base cove that extends up the wall.



The flooring installed in the shared kitchenette between 0-3 and 3-5 years daycare rooms



Flooring and a glimpse of things coming together in the 3-5 year daycare room



Without delay, floor protection is installed to protect the flooring during the finishing phases of construction. HVAC and electrical work continues in the main corridor.



While the finishing progresses on the inside, excavation, drain tile installation, backfill and compaction work progresses outside.

Insulation is completed on the foundation wall, and concrete faced insulation is installed on the top level of foundation to give a finished look.



Backfill nearing completion on the N side of the building. Final grading, and sidewalks, as well as the siding are still to be completed.



A lock-Block retaining is being installed on the S, W and N perimeter of the daycare to achieve finished grade and preparation for the sidewalk installation.

The new grading and sidewalks will eliminate any stairs making the school and daycare accessible to everyone
